


INCOR PBEL CITY PHASE 3 - CHENNAI

B5-Marbella:


Week-1



UG wall reinforcement distribution works in progress. wall shuttering board making works in progress

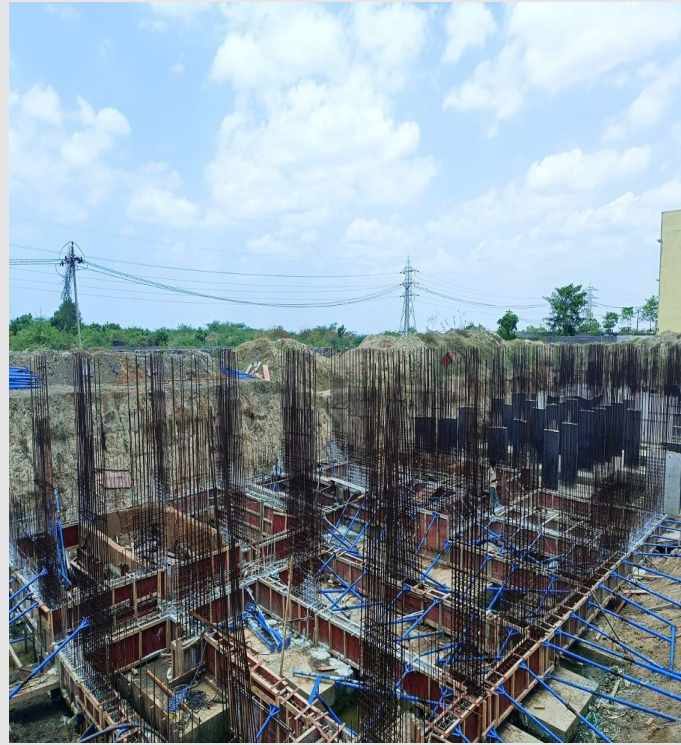

UG sump plinth beam concrete completed. waterproofing dimple board protection sheet works in progress

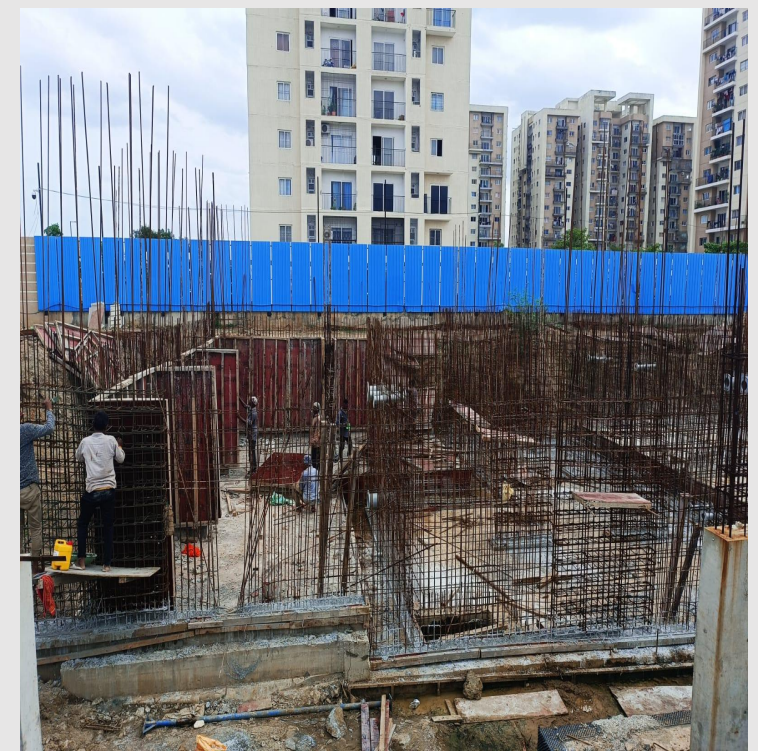

UG Sump pump room and fire sump wall starter concrete completed and pedal flange fixing works and sump wall shuttering works in progress

B5-Marbella:

Week 2



Ug sump wall shuttering works and plinth beam. PCC Soil leveling works



UG Sump wall shuttering work and plinth beam PCC Preparation work, stilt floor column reinforcement work

B6-Trinity:

Week 1



Footing RCC 82cum concrete in progress.
column shuttering works in progress



Footing and column reinforcement and footing shuttering works in progress. footing and column curing work in progress. 5nos footing concrete work in progress

B6-Trinity:

Week-2



Footing and column reinforcement and shuttering works in progress.
7nos column concrete planned



footing PCC concrete work



Footing and column reinforcement work and shuttering work in progress.
4nos footing concrete work in progress

C1-Newport:

Week-1



North side 2nd lift column shuttering works in progress. south side waterproofing coating preparation works in progress



Column 2nd lift 7nos concrete completed and column shuttering making work in progress. column and sump wall tie rod hole pipe removal work in progress

C1-Newport:

Week-2:



Column 2nd lift shuttering works in progress, today 2nd lift column 7nos concrete planned backfilling and waterproofing coating preparation works in progress



Column 2nd lift concrete work



Column 2nd lift shuttering work. Backfilling works and waterproofing coating preparation work in progress

C2-Destin:

Week-1



footing PCC Preparation works in progress



Footing PCC Preparation works in progress

C2-Destin:

Week-2



Footing PCC work in progress



Footing PCC Works in progress

C3-Miramar:

Week-1



Excavation 2.5m depth completed



Excavation work in progress

C3-Miramar:

Week-2



Excavation works in progress



Excavation work in progress

C6-Maho:

Week-2:



excavation preparation work in progress

E1-Malta:

Week-2



Plinth beam shuttering work



plinth beam concrete work

E1-Malta:

Week 2



waterproofing works in footing and column in progress. backfilling works in progress



Waterproofing coating preparation work in progress
