


INCOR PBEL CITY PHASE 3 - CHENNAI

B5-Marbella

Week-1



UG sump raft concrete work

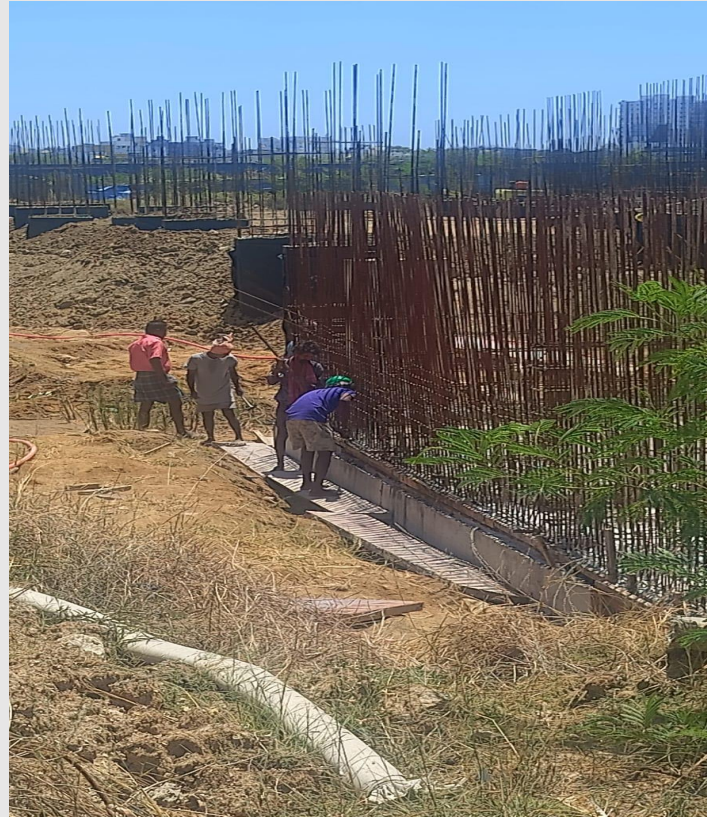

UG sump deshuttering work in progress



UG sump concreting work completed & Curing in progress

B6 -Trinity & C3 - Miramar:

Week-1



Dewatering work in progress

C1-Newport:

Week-1



North side soil levelling and roller compaction works in progress



U G sump pump room shuttering works in progress

E1-Malta:

Week-1



South side waterproofing completion
area 1st layer soil filling works in
progress

B5-Marbella

Week-2:



Soil backfilling & compaction work in progress



Soil test work in progress

B6 -Trinity

Week-2:



Slush cleaning work in progress

C1-Newport:

Week-2:



U G sump area pump room shuttering works in progress
North side 3rd layer soil compaction 3rd party testing will done
today second half.

E1-Malta:

Week-2:



1st layer soil levelling and roller compaction works in progress

B6-Trinity:

Week -3:



Slush Cleaning work in progress

C1-Newport:

Week -3:



UG sump pump room and 13 column shuttering and supporting works in progress

E1-Malta:

Week -3:



waterproofing purpose footing side soil and
sludge removing works in progress

B6-Trinity:


Week-4:



Footing PCC works in progress



pcc preparation work in progress.&
Footing reinforcement making in
progress

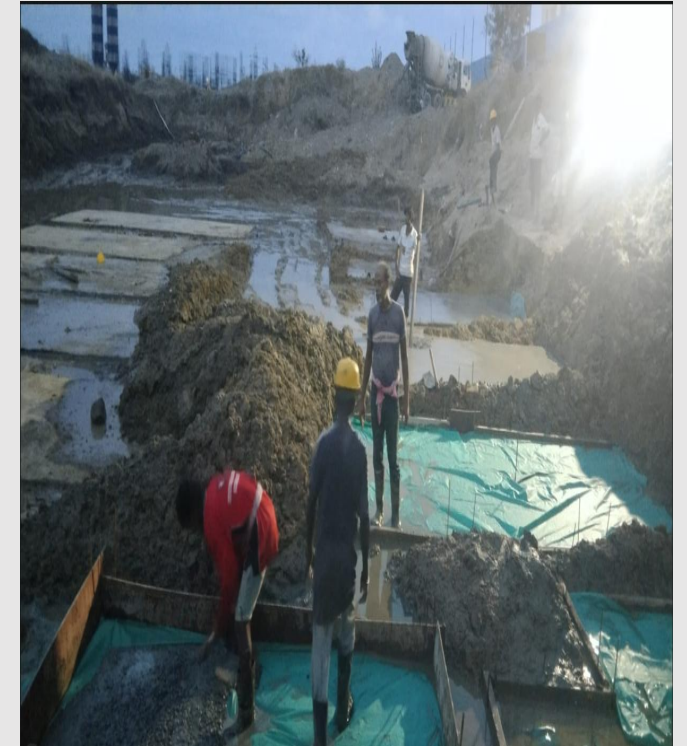

footing PCC in progress

C1-Newport:

Week-4:



UG sump pump room & 13 nos column shuttering supporting and scaffolding works in progress



UG sump pump room and 13nos of column shuttering and supporting works in progress

E1-Malta:

Week-4:



Sludge cleaning for waterproofing works in progress
